

NUCLEAR COMPACTION TEST REPORT FOR BASE AGGREGATE

PROJECT NAME (SECTION) VA Cemetery Roseburg		CONTRACT NUMBER	
CONTRACTOR OR SUPPLIER HCC Construction		PROJECT MANAGER	
PANEL WIDTH Varies	LIFT THICKNESS Varies	TYPE GAUGE-SERIAL NUMBER Troxler 3430	BID ITEM NUMBER
			MIX NOMINAL SIZE 3/4"-0

ROLLER TYPE AND DESCRIPTION (MANUFACTURE, WEIGHT, ETC)

Peanut roller

TEST NUMBER	1	2	3	4	5
DATE OF TEST	4/17/2025	4/17/2025	4/17/2025	4/17/2025	4/17/2025
TEST LOCATION (STATION)	See				
DISTANCE LT. OR RT. OF CENTERLINE (FEET)	Diagram				
SOURCE POSITION	6"	6"	6"	6"	6"
LIFT	Top	Top	Top	Top	Top
WET DENSITY MAX DIFFERENCE 2 lb/ft³	1D	124.7	132.3	118.1	134.6
	2D	124.7	132.3	118.1	134.6
MOISTURE	1M	6.8	7.4	6.0	7.4
	2M	6.8	7.4	6.0	7.4
AVE. WET DENSITY	AD	124.7	132.3	118.1	134.6
AVE. MOISTURE	AM	6.8	7.4	6	7.4
DRY DENSITY (AD-AM)	DD	117.9	124.9	112.1	127.2
% MOISTURE (AM / DD) x 100	%M	5.8%	5.9%	5.4%	5.8%
Curve #	1	1	1	1	1
Source #	OR 10-238-3	OR 10-238-3	OR 10-238-3	OR 10-238-3	OR 10-238-3
RELATIVE MAXIMUM DRY DENSITY ρ_d	133.4	133.4	133.4	133.4	133.4
Combined Optimum Moisture	8.5%	8.5%	8.5%	8.5%	8.5%
% COMPACTION FOR INDIVIDUAL TESTS $(DD / \rho_d) \times 100$	% REQ	88%	94%	84%	95%
				95%	93%

CHECK APPROPRIATE ☐

MATERIAL DEFLECTED UNDER LOADED EQUIPMENT ☐

MATERIAL DID NOT DEFLECT UNDER LOADED EQUIPMENT ☐

REPRESENTS MATERIAL INCORPORATED

FROM STATION


TO STATION

FROM OFFSET

TO OFFSET

REMARKS

1 test per location- numbers duplicated to show failing test percentages
Material was of variable thickness and not extended to full width of projected pad area.

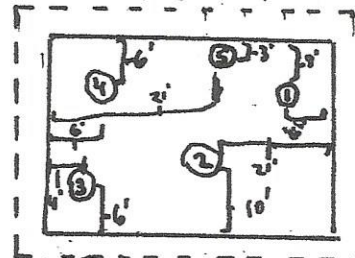

☒ QUALITY CONTROL	☐ VERIFICATION	
CERTIFIED TECHNICIAN (PLEASE PRINT) AND CARD NUMBER Patrick Tanner #49817	COMPANY NAME Testing Service	SIGNATURE DATE 4/17/2025
