

Project ID(s): Annual Medical Gas Inspection
Project Date(s): 1/05/2026

Evergreen Medical Services

Corporate Headquarters
8047 Castleton Road
Indianapolis, IN 46250
800-727-8321
www.EvergreenMedical.com

MEDICAL GAS SYSTEMS MAINTENANCE INSPECTION

Project ID(s): Annual Medical Gas Inspection
Project Date(s): 1/05/2026
Tested to NFPA 99: 2018



Report Authored By: Erick Siela

ASSE Credential #: 02152407

Project Site:

VA Medical Center - Fort Wayne
2121 Lake Ave
Fort Wayne, IN 46805

Project Contact:

Michael Foster
Facilities
(260) 421-1062
michael.foster7@va.gov

MEDICAL GAS SYSTEMS MAINTENANCE INSPECTION

PURPOSE

The inspection and testing documented in this report is designed around satisfying the medical gas systems maintenance program requirements laid out in NFPA 99 section 5.1.14. The purpose driving these maintenance program requirements is to ensure that medical gas system components are compliant with applicable NFPA 99 codes and standards, remain in good repair, and are operating within manufacturer specifications or recommendations.

SCOPE AND APPLICATION

Per NFPA 99, the maintenance, inspection and testing operations of medical gas systems apply to all facilities—new and existing—with Category 1-3 Medical Gas, Vacuum, WAGD, and Medical Support Gas systems.

TESTING & INSPECTION PROCEDURES

EMS has designed its testing & inspection scope and procedure around applicable NFPA 99 codes and pertinent inspection and accreditation requirements, and manufacturer recommendations following industry best practices. However, your facility's risk assessment committee has the ultimate responsibility in deciding the scope and frequency of scheduled inspections for medical gas components and the associated procedures. These inspections are to be developed with consideration of the original equipment manufacturer recommendations and other recommendations as required by the authority having jurisdiction.

The testing & inspection procedures represented in this report are as follows unless otherwise directed and document by the facility's risk assessment team:

Facility testing and system evaluation performed to be in compliance with NFPA 99 2018 Edition.

MASTER ALARMS :

Master alarm panel location is recorded along with manufacturer and model of alarm and location of initiating device. Master alarm panels are tested for proper audible and visual alarm activation & deactivation, each signal is inspected for proper labeling and wiring is inspected for independence to initiating device.

All master alarm signals* are tested by simulating each alarm condition and/or actuating the signal at the initiating device wherever possible.

If it is not possible to simulate an alarm condition or actuate the signal by changing system conditions then the alarm's wiring will be tested for continuity from the initiating to the master alarm panels.

**Cryogenic liquid central supply system master alarm signals that terminate within the supplier-owned equipment are not tested per the EMS maintenance inspection SOP as such signals are required to be tested by the supplier/equipment owner annually and EMS views this testing as sufficient in satisfying the NFPA 99 inspection requirement. EMS can test these signals per request, however the facility will have to direct the method used to perform this testing.*

AREA ALARMS :

Area alarm panel location and area monitored is recorded along with manufacturer and model of alarm. Area alarm panels are tested for proper audible and visual alarm activation and deactivation through use of the alarm "test" function. Condition of area alarm and components are inspected.

System gas, high & low alarm setpoints are recorded and pressure reading is recorded and tested for accuracy.

Area monitored labeling and transducer location can only be verified by tracing piping and/or altering zone pressure. Actual alarm function under alarm conditions (high or low pressure) can only be verified by altering zone pressure. These tests can be performed by request but are not included in EMS's maintenance inspection SOP.

VALVES :

Valve location and labeling (including area(s) served, system gas and other required verbiage), manufacturer, valve type and pressure reading are inspected and recorded. Gauge pressure is recorded and tested for accuracy. Condition of valve assembly and enclosure are inspected and valves are checked for leaks.

Area served labeling can only be verified by tracing piping and/or altering zone pressure. This test can be performed by request but is not included in EMS's maintenance inspection SOP.

OUTLETS & INLETS :

Outlet or inlet location, manufacturer, model, position and labeling is inspected and recorded. Outlets/inlets are tested for proper connect & release, leaks and general condition.

One outlet/inlet per zone is tested for static pressure and compared with zone valve gauge reading and/or area alarm pressure reading.

All outlets/inlets are tested for dynamic pressure/operational flow pressure drop.

All positive pressure medical gases are tested for oxygen concentration as a way of determining if existing cross-connections between two medical gases exist.

MEDICAL GAS SYSTEMS MAINTENANCE INSPECTION

GAS CONTAMINANTS :

Particulate Contaminants - A representative sampling of each gas system pipeline is tested for particulate contaminants using a 0.45 micron filter membrane connected to an outlet of each gas. Results of this test are then recorded.

Dew Point - A representative sampling of medical air and instrument air pipeline is tested for dew point using a portable dew point monitor connected to an outlet of each gas. Results of this test are then recorded.

Odor - All positive pressure outlets are tested for objectionable or pronounced odor and the results are then recorded.

Gaseous Contaminants - Testing each gas system pipeline and source for total nonmethane hydrocarbons and halogenated hydrocarbons can be performed by request but is not included in EMS's maintenance inspection SOP.

SOURCE EQUIPMENT :

All source systems' manufacturer, model number and specifications are recorded. Proper functioning of each system is observed and recorded. Each source type is inspected based on the associated inspection checklist visible on the page(s) of this report specific to that source system.

QUALIFICATIONS

EMS service technicians are qualified to perform medical gas systems inspections and maintenance to one or more of the following qualification requirements per NFPA 99 5.1.14:

- 1) Documented training by which such persons are qualified to work with specific equipment as installed in that facility.
- 2) Credentialing to the requirements of ASSE 6040, Professional Qualification Standard for Medical Gas Maintenance Personnel.
- 3) Credentialing to the requirements of ASSE 6030, Professional Qualification Standard for Medical Gas Systems Verifiers.

TECHNICIAN CREDENTIALS





Evergreen Medical Services has evaluated the medical piping systems indicated in this report in accordance with applicable NFPA 99 Health Care Facilities Code and ASSE 6000 Standards. These systems have been found to be within applicable guidelines except as noted within this report. Any deficiencies cited are based on the most applicable edition of NFPA 99. See coversheet for relevant NFPA 99 edition.

Per NFPA 99 an existing system that is not in strict compliance with the applicable codes may continue to be used as long as it is not a distinct hazard to safety. Fire/explosion hazards, labeling, manifold enclosures, medical air usage, & maintenance codes apply to new & existing facilities.

The information recorded in this report represents the state of the medical gas systems for the indicated inspection date(s) only. Any action taken in response to recommendations included in this report should be recorded on the appropriate pages. This report should not be copied unless in its entirety.

TABLE OF CONTENTS	
■	Summary of Findings
■	Master Alarms
■	Area Alarms
■	Valves
■	Outlets & Inlets
■	Contaminants
■	Source Equipment
■	Annex

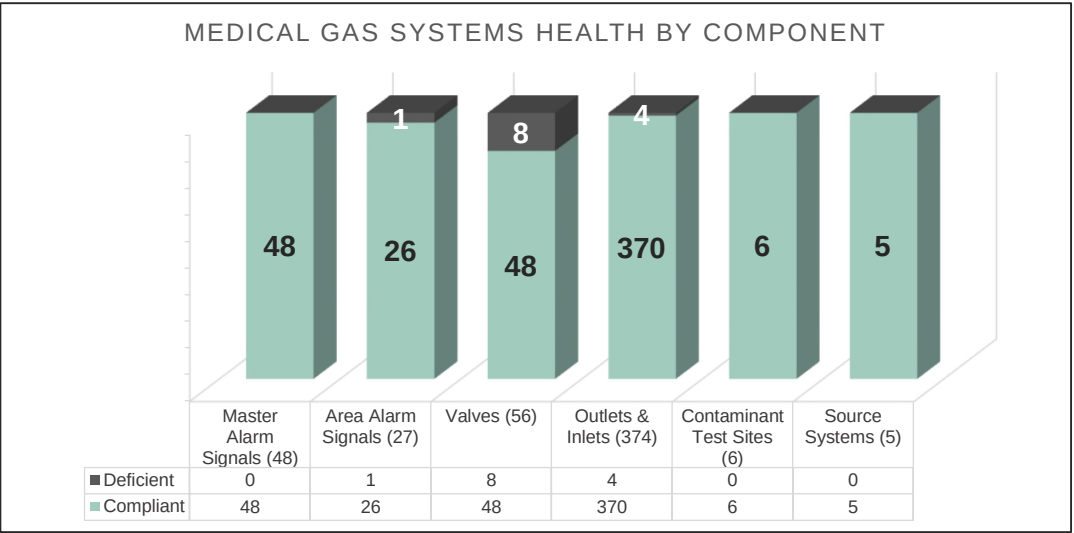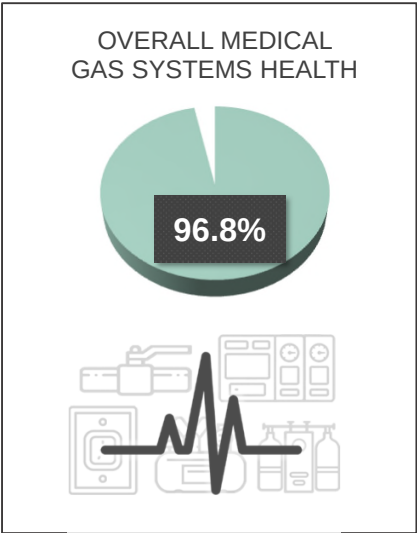

SUMMARY OF DEFICIENCIES

Individual deficiencies and corrective action notes can be found in the component sections ('Master Alarms', 'Area Alarms', 'Valves', 'Outlets & Inlets', 'Contaminants', 'Sources & Pipeline'). This summary provides an overview of deficiency or corrective action type, location and quantity. For discussion regarding what constitutes a deficiency, please note the "Scope & Procedures" section of this report. For findings that have not been marked as deficient but instead EMS has provided a recommendation, please note the "Annex" section of this report.

MASTER ALARMS

No deficiencies at time of test

No corrective action reported

AREA ALARMS

DEFICIENCY DETAIL - AREA ALARMS	ALARM PANEL LOCATION(S)	QTY
No Alarm Panel Installed Serving 3204 Recovery	0	1

CORRECTIVE ACTION DETAIL - AREA ALARMS	ALARM PANEL LOCATION(S)	QTY
No corrective action reported		

VALVES

DEFICIENCY DETAIL - VALVES	VALVE LOCATION(S)	QTY
No Intervening Wall Between Zone Valves and Outlets / Inlets Served	3rd Floor: Rm 3315, 3rd Floor: Rm 3304 (Pre-Op)	6
No Nitrogen Valve Installed Serving OR 3232	0	1
No Nitrogen Valve Installed Serving OR 3235	0	1

CORRECTIVE ACTION DETAIL - VALVES	VALVE LOCATION(S)	QTY
No corrective action reported		

OUTLET & INLETS

DEFICIENCY DETAIL - OUTLETS & INLETS	OUTLET/INLET LOCATION(S) / ASSET #	QTY
WAGD Inlet Required (Anesthetizing Location)	3rd Floor 3210, 3rd Floor 3218, 3rd Floor 3232, 3rd Floor 3235	4

CORRECTIVE ACTION DETAIL - OUTLETS & INLETS	OUTLET/INLET LOCATION(S) / ASSET #	QTY
No corrective action reported		

GAS CONTAMINANTS

No deficiencies at time of test

No corrective action reported

SOURCE EQUIPMENT

No deficiencies at time of testing

No corrective action reported

TOTAL MASTER ALARM SIGNALS	48	MASTER ALARM SIGNALS BY SYSTEM GAS:	18 12 6 6 0 6 0 0 0								
		TOTAL MASTER ALARM PANELS:	3								
MASTER ALARMS BREAKDOWN (*EACH MASTER ALARM SIGNAL COUNTED AS SEPARATE ALARM BY SYSTEM GAS BELOW)											
MANUFACTURER	MODEL	MASTER ALARM PANEL DESCRIPTION	O2	MA	N2O	N2	CO2	VAC	WAGD	IA	Other
Amico	A2M	Gray Cover with Red LED Indicators	18	12	6	6		6			

MASTER ALARMS: LOCATION & SPECIFICATION							FUNCTION & CONDITION			
#	Master Alarm Panel Location/## *If multiple panels per location (e.g. "Engineering Panel 1")	System	MFR	Model	Condition Monitored	Switch or Source Location	Set Point	Unit of Measure	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
1	ER	N2O	Amico	A2M	Line Pressure Low	Manifold Room			PASS	
2	ER	N2O	Amico	A2M	Line Pressure High	Manifold Room			PASS	
3	ER	N2O	Amico	A2M	Reserve In Use	Manifold Room			PASS	
4	ER	N2	Amico	A2M	Line Pressure Low	Manifold Room			PASS	
5	ER	N2	Amico	A2M	Line Pressure High	Manifold Room			PASS	
6	ER	N2	Amico	A2M	Reserve In Use	Manifold Room			PASS	
7	ER	O2	Amico	A2M	Liquid Level Low	Outside Mailroom - In Basement Ceiling			SEE ANNEX	Tested by Bulk Supplier
8	ER	O2	Amico	A2M	Reserve Cylinder In Use	Outside Mailroom - In Basement Ceiling			SEE ANNEX	Tested by Bulk Supplier
9	ER	O2	Amico	A2M	Emergency Cylinder Low	Outside Mailroom - In Basement Ceiling			SEE ANNEX	Alarm Not Required (Liq x Gas)
10	ER	O2	Amico	A2M	Reserve Gas Pressure Low	Outside Mailroom - In Basement Ceiling			SEE ANNEX	Tested by Bulk Supplier
11	ER	O2	Amico	A2M	Line Pressure Low	Outside Mailroom - In Basement Ceiling			PASS	Tested At Panel
12	ER	O2	Amico	A2M	Line Pressure High	Outside Mailroom - In Basement Ceiling			PASS	Tested At Panel
13	ER	MA	Amico	A2M	Compressor Maintenance Required	Mechanical Room Penthouse			PASS	
14	ER	MA	Amico	A2M	High Dew Point	Mechanical Room Penthouse			PASS	
15	ER	MA	Amico	A2M	Line Pressure Low	Mechanical Room Penthouse			PASS	
16	ER	MA	Amico	A2M	Line Pressure High	Mechanical Room Penthouse			PASS	
17	ER	VAC	Amico	A2M	Low	Mechanical Room Penthouse			PASS	
18	ER	VAC	Amico	A2M	Pumps Maintenance Required	Mechanical Room Penthouse			PASS	

MASTER ALARMS: LOCATION & SPECIFICATION							FUNCTION & CONDITION			
#	Master Alarm Panel Location/## *If multiple panels per location (e.g. "Engineering Panel 1")	System	MFR	Model	Condition Monitored	Switch or Source Location	Set Point	Unit of Measure	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
19	Maintenance	N2O	Amico	A2M	Line Pressure Low	Manifold Room			PASS	
20	Maintenance	N2O	Amico	A2M	Line Pressure High	Manifold Room			PASS	
21	Maintenance	N2O	Amico	A2M	Reserve In Use	Manifold Room			PASS	PASS
22	Maintenance	N2	Amico	A2M	Line Pressure Low	Manifold Room			PASS	
23	Maintenance	N2	Amico	A2M	Line Pressure High	Manifold Room			PASS	
24	Maintenance	N2	Amico	A2M	Reserve In Use	Manifold Room			PASS	
25	Maintenance	O2	Amico	A2M	Liquid Level Low	Outside Mailroom - In Basement Ceiling			SEE ANNEX	Tested by Bulk Supplier
26	Maintenance	O2	Amico	A2M	Reserve Cylinder In Use	Outside Mailroom - In Basement Ceiling			SEE ANNEX	Tested by Bulk Supplier
27	Maintenance	O2	Amico	A2M	Emergency Cylinder Low	Outside Mailroom - In Basement Ceiling			SEE ANNEX	Alarm Not Required (Liq x Gas)
28	Maintenance	O2	Amico	A2M	Reserve Gas Pressure Low	Outside Mailroom - In Basement Ceiling			SEE ANNEX	Tested by Bulk Supplier
29	Maintenance	O2	Amico	A2M	Line Pressure Low	Outside Mailroom - In Basement Ceiling			PASS	Tested At Panel
30	Maintenance	O2	Amico	A2M	Line Pressure High	Outside Mailroom - In Basement Ceiling			PASS	Tested At Panel
31	Maintenance	MA	Amico	A2M	Compressor Maintenance Required	Mechanical Room Penthouse			PASS	
32	Maintenance	MA	Amico	A2M	High Dew Point	Mechanical Room Penthouse			PASS	
33	Maintenance	MA	Amico	A2M	Line Pressure Low	Mechanical Room Penthouse			PASS	
34	Maintenance	MA	Amico	A2M	Line Pressure High	Mechanical Room Penthouse			PASS	
35	Maintenance	VAC	Amico	A2M	Low	Mechanical Room Penthouse			PASS	
36	Maintenance	VAC	Amico	A2M	Pumps Maintenance Required	Mechanical Room Penthouse			PASS	

MASTER ALARMS: LOCATION & SPECIFICATION							FUNCTION & CONDITION			
#	Master Alarm Panel Location/## *If multiple panels per location (e.g. "Engineering Panel 1")	System	MFR	Model	Condition Monitored	Switch or Source Location	Set Point	Unit of Measure	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
37	4th Floor	O2	Amico	A2M	Liquid Level Low	Outside Mailroom - In Basement Ceiling			SEE ANNEX	Tested By Bulk Supplier
38	4th Floor	O2	Amico	A2M	Reserve Cylinder In Use	Outside Mailroom - In Basement Ceiling			SEE ANNEX	Tested By Bulk Supplier
39	4th Floor	O2	Amico	A2M	Emergency Cylinder Low	Outside Mailroom - In Basement Ceiling			SEE ANNEX	Alarm Not Required (Liq x Gas)
40	4th Floor	O2	Amico	A2M	Reserve Gas Pressure Low	Outside Mailroom - In Basement Ceiling			SEE ANNEX	Tested By Bulk Supplier
41	4th Floor	O2	Amico	A2M	Line Pressure Low	Outside Mailroom - In Basement Ceiling			PASS	Tested At Pane
42	4th Floor	O2	Amico	A2M	Line Pressure High	Outside Mailroom - In Basement Ceiling			PASS	Tested At Panel
43	4th Floor	MA	Amico	A2M	Compressor Maintenance Required	Mechanical Room Penthouse			PASS	
44	4th Floor	MA	Amico	A2M	High Dew Point	Mechanical Room Penthouse			PASS	
45	4th Floor	MA	Amico	A2M	Line Pressure Low	Mechanical Room Penthouse			PASS	
46	4th Floor	MA	Amico	A2M	Line Pressure High	Mechanical Room Penthouse			PASS	
47	4th Floor	VAC	Amico	A2M	Low	Mechanical Room Penthouse			PASS	
48	4th Floor	VAC	Amico	A2M	Pumps Maintenance Required	Mechanical Room Penthouse			PASS	

TOTAL AREA ALARM SIGNALS	27	TOTAL AREA ALARM SIGNALS BY SYSTEM GAS:	971109000								
		TOTAL AREA ALARM PANELS:	9								
AREA ALARMS BREAKDOWN (EACH AREA ALARM SIGNAL COUNTED AS SEPARATE ALARM BY SYSTEM GAS BELOW)											
MANUFACTURER (Or Current Parent Company)	MODEL	AREA ALARM DESCRIPTION	O2	MA	N2O	N2	CO2	VAC	WAGD	IA	Other
Amico			1		1	1		1			
Amico	Alert		1	1				1			
Amico	LCD		6	6				6			
Puritan Bennett	Mega		1					1			

AREA ALARMS: LOCATION & SPECIFICATION						FUNCTION AND CONDITION				
#	Physical Location	Area/Rooms Monitored	System	MFR	Model	Pressure Reading (All Gases PSI/ VAC & WAGD inHg)	High Pressure Setting (All Gases PSI/ VAC & WAGD inHg)	Low Pressure Setting (All Gases PSI/ VAC & WAGD inHg)	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
1	1st Floor: ER A 139, A 141 - A 153, A 103 - A 136	ER A 139, A 141 - A 153, A 103 - A 136	O2	Puritan Bennett	Mega				PASS	Recommend Verifying Areas Served and Relabel
2	1st Floor: ER A 139, A 141 - A 153, A 103 - A 136	ER A 139, A 141 - A 153, A 103 - A 136	VAC	Puritan Bennett	Mega				PASS	Recommend Verifying Areas Served and Relabel
3	2nd Floor: Room 203 & 207 (Located In Office)	Room 203 & 207	O2	Amico	Alert				PASS	
4	2nd Floor: Room 203 & 207 (Located In Office)	Room 203 & 207	MA	Amico	Alert				PASS	
5	2nd Floor: Room 203 & 207 (Located In Office)	Room 203 & 207	VAC	Amico	Alert				PASS	
6	3rd Floor: 3315	3315	O2	Amico	LCD				PASS	
7	3rd Floor: 3315	3315	MA	Amico	LCD				PASS	
8	3rd Floor: 3315	3315	VAC	Amico	LCD				PASS	
9	3rd Floor: ORs / Surgery (Located In Room 3213)	ORs / Surgery	O2	Amico					PASS	
10	3rd Floor: ORs / Surgery (Located In Room 3213)	ORs / Surgery	VAC	Amico					PASS	
11	3rd Floor: ORs / Surgery (Located In Room 3213)	ORs / Surgery	N2O	Amico					PASS	
12	3rd Floor: ORs / Surgery (Located In Room 3213)	ORs / Surgery	N2	Amico					PASS	
13	3rd Floor: 3315B - 3315D	3315B - 3315D	O2	Amico	LCD				PASS	
14	3rd Floor: 3315B - 3315D	3315B - 3315D	MA	Amico	LCD				PASS	
15	3rd Floor: 3315B - 3315D	3315B - 3315D	VAC	Amico	LCD				PASS	
16	3rd Floor: Rm 3304 (Pre-Op)	Rm 3304 (Pre-Op)	O2	Amico	LCD				PASS	
17	3rd Floor: Rm 3304 (Pre-Op)	Rm 3304 (Pre-Op)	MA	Amico	LCD				PASS	
18	3rd Floor: Rm 3304 (Pre-Op)	Rm 3304 (Pre-Op)	VAC	Amico	LCD				PASS	
		3rd Floor: 3204 Recovery							FAIL	No Alarm Panel Installed Serving 3204 Recovery
19	4th Floor: 4312, 4316, 4320, 4324, 4326, 4333, 4332, 4346, 4348	4312, 4316, 4320, 4324, 4326, 4333, 4332, 4346, 4348	O2	Amico	LCD				PASS	
20	4th Floor: 4312, 4316, 4320, 4324, 4326, 4333, 4332, 4346, 4348	4312, 4316, 4320, 4324, 4326, 4333, 4332, 4346, 4348	MA	Amico	LCD				PASS	
21	4th Floor: 4312, 4316, 4320, 4324, 4326, 4333, 4332, 4346, 4348	4312, 4316, 4320, 4324, 4326, 4333, 4332, 4346, 4348	VAC	Amico	LCD				PASS	

AREA ALARMS: LOCATION & SPECIFICATION						FUNCTION AND CONDITION				
#	Physical Location	Area/Rooms Monitored	System	MFR	Model	Pressure Reading (All Gases: PSI / VAC & WAGD inHg)	High Pressure Setting (All Gases: PSI / VAC & WAGD inHg)	Low Pressure Setting (All Gases: PSI / VAC & WAGD inHg)	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
22	4th Floor: (ICU) 4353, 4352, 4364, 4365	(ICU) 4353, 4352, 4364, 4365	O2	Amico	LCD				PASS	
23	4th Floor: (ICU) 4353, 4352, 4364, 4365	(ICU) 4353, 4352, 4364, 4365	MA	Amico	LCD				PASS	
24	4th Floor: (ICU) 4353, 4352, 4364, 4365	(ICU) 4353, 4352, 4364, 4365	VAC	Amico	LCD				PASS	
25	4th Floor: 4102 - 4160	4102 - 4160	O2	Amico	LCD				PASS	
26	4th Floor: 4102 - 4160	4102 - 4160	MA	Amico	LCD				PASS	
27	4th Floor: 4102 - 4160	4102 - 4160	VAC	Amico	LCD				PASS	

TOTAL VALVES	56	TOTAL VALVES BY SYSTEM GAS:	22 8 5 1 0 20 0 0 0									
		TOTAL ZONE VALVE BOXES	24									

VALVES BREAKDOWN (EACH SYSTEM GAS COUNTED AS SEPARATE ZONE VALVE)

MANUFACTURER	VALVE TYPE	VALVE DESCRIPTION	O2	MA	N2O	N2	CO2	VAC	WAGD	IA	Other
Amico	Zone - 1/4 Turn	Accessible valve through which all station outlets/inlets are served	6	5				6			
Beacon	Zone - 1/4 Turn	Accessible valve through which all station outlets/inlets are served	1	1				1			
NCG	Zone - 1/4 Turn	Accessible valve through which all station outlets/inlets are served	12	1	5	1		9			
Ohmeda	Zone - 1/4 Turn	Accessible valve through which all station outlets/inlets are served		1				1			
Puritan Bennett	Service - 1/4 Turn	For servicing or modification of lateral branch piping	1								
Puritan Bennett	Zone - 1/4 Turn	Accessible valve through which all station outlets/inlets are served	2					3			

VALVES: LOCATION & SPECIFICATION						FUNCTION AND CONDITION		
#	Physical Location	Area/Rooms Served	System	MFR	Valve Type	Gauge Reading (All Gases PSI/ VAC & WAGD inHg)	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
1	1st Floor: A 103 - A 136	A 103 - A 136	VAC	Puritan Bennett	Zone - 1/4 Turn		PASS	
2	1st Floor: A 153, A 141 - A 143, A 148 - A 153	A 153	O2	Puritan Bennett	Zone - 1/4 Turn		PASS	
3	1st Floor: A 153, A 141 - A 143, A 148 - A 153	A 141 - A 143, A 148 - A 153	VAC	Puritan Bennett	Zone - 1/4 Turn		PASS	Recommend Verifying Areas Served and Relabel
4	1st Floor: Room A 139	Room A 139	O2	Puritan Bennett	Zone - 1/4 Turn		PASS	
5	1st Floor: Room A 139	Room A 139	VAC	Puritan Bennett	Zone - 1/4 Turn		PASS	
6	1st Floor: Room 167	Room 167	O2	Beacon	Zone - 1/4 Turn		PASS	
7	1st Floor: Room 167	Room 167	MA	Beacon	Zone - 1/4 Turn		PASS	
8	1st Floor: Room 167	Room 167	VAC	Beacon	Zone - 1/4 Turn		PASS	
9	2nd Floor: Room 203 & 207 (In Hallway Near Restrooms)	Room 203 & 207	O2	NCG	Zone - 1/4 Turn		PASS	
10	2nd Floor: Room 203 & 207 (In Hallway Near Restrooms)	Room 203 & 207	MA	NCG	Zone - 1/4 Turn		PASS	
11	2nd Floor: Room 203 & 207 (In Hallway Near Restrooms)	Room 203 & 207	VAC	NCG	Zone - 1/4 Turn		PASS	
12	3rd Floor: OR 3218	OR 3218	O2	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
13	3rd Floor: OR 3218	OR 3218	VAC	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
14	3rd Floor: OR 3218	OR 3218	N2O	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
		OR 3218					SEE ANNEX	No Nitrogen Valve Installed Serving OR 3218; N2 Outlets Not In Service
15	3rd Floor: OR 3232	OR 3232	O2	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
16	3rd Floor: OR 3232	OR 3232	VAC	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
17	3rd Floor: OR 3232	OR 3232	N2O	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
		OR 3232					FAIL	No Nitrogen Valve Installed Serving OR 3232
18	3rd Floor: OR 3235	OR 3235	O2	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
19	3rd Floor: OR 3235	OR 3235	VAC	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
20	3rd Floor: OR 3235	OR 3235	N2O	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
		OR 3235					FAIL	No Nitrogen Valve Installed Serving OR 3235

VALVES: LOCATION & SPECIFICATION						FUNCTION AND CONDITION		
#	Physical Location	Area/Rooms Served	System	MFR	Valve Type	Gauge Reading (All Gases PSU VAC & WAGD inHg)	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
21	3rd Floor: 3 West Service Valve	3 West Service Valve	O2	Puritan Bennett	Service - 1/4 Turn		UNAVAILABLE	Under Construction
22	3rd Floor: 3133, 3134, 3135, 3137, 3138, 3139 (Box 1)	3133, 3134, 3135, 3137, 3138, 3139	O2	NCG	Zone - 1/4 Turn		UNAVAILABLE	Under Construction
23	3rd Floor: 3133, 3134, 3135, 3137, 3138, 3139 (Box 2)	3133, 3134, 3135, 3137, 3138, 3139	MA	Ohmeda	Zone - 1/4 Turn		UNAVAILABLE	Under Construction
24	3rd Floor: 3133, 3134, 3135, 3137, 3138, 3139 (Box 2)	3133, 3134, 3135, 3137, 3138, 3139	VAC	Ohmeda	Zone - 1/4 Turn		UNAVAILABLE	Under Construction
25	3rd Floor: 335 - 340	335 - 340	O2	NCG	Zone - 1/4 Turn		UNAVAILABLE	Under Construction
26	3rd Floor: 331 - 332	331 - 332	O2	NCG	Zone - 1/4 Turn		UNAVAILABLE	Under Construction
27	3rd Floor: 3315 D	3315 D	O2	NCG	Zone - 1/4 Turn		PASS	
28	3rd Floor: 3315 D	3315 D	VAC	NCG	Zone - 1/4 Turn		PASS	
29	3rd Floor: 302 - 313 (Master Shut Off - Box 1)	302 - 313 (Master Shut Off)	O2	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
30	3rd Floor: 302 - 313 (Master Shut Off - Box 2)	302 - 313 (Master Shut Off)	VAC	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
31	3rd Floor: 3204 (Recovery)	3204 (Recovery)	O2	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
32	3rd Floor: 3204 (Recovery)	3204 (Recovery)	VAC	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
33	3rd Floor: OR 3208	OR 3208	O2	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
34	3rd Floor: OR 3208	OR 3208	VAC	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
35	3rd Floor: OR 3208	OR 3208	N2O	NCG	Zone - 1/4 Turn		NOT IN USE	
36	3rd Floor: OR 3208	OR 3208	N2	NCG	Zone - 1/4 Turn		NOT IN USE	
37	3rd Floor: OR 3210	OR 3210	O2	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
38	3rd Floor: OR 3210	OR 3210	VAC	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
39	3rd Floor: OR 3210	OR 3210	N2O	NCG	Zone - 1/4 Turn		SEE ANNEX	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard
		OR 3210					SEE ANNEX	No Nitrogen Valve Installed Serving OR 3210; N2 Outlets Not In Service
40	3rd Floor: Rm 3315	Rm 3315	O2	Amico	Zone - 1/4 Turn		FAIL	No Intervening Wall Between Zone Valves and Outlets / Inlets Served
41	3rd Floor: Rm 3315	Rm 3315	MA	Amico	Zone - 1/4 Turn		FAIL	No Intervening Wall Between Zone Valves and Outlets / Inlets Served
42	3rd Floor: Rm 3315	Rm 3315	VAC	Amico	Zone - 1/4 Turn		FAIL	No Intervening Wall Between Zone Valves and Outlets / Inlets Served
43	3rd Floor: 3315B	3315B	O2	Amico	Zone - 1/4 Turn		PASS	
44	3rd Floor: 3315B	3315B	VAC	Amico	Zone - 1/4 Turn		PASS	

VALVES: LOCATION & SPECIFICATION						FUNCTION AND CONDITION		
#	Physical Location	Area/Rooms Served	System	MFR	Valve Type	Gauge Reading (All Gases PSI/ VAC & WAGD inHg)	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
45	3rd Floor: Rm 3304 (Pre-Op)	Rm 3304 (Pre-Op)	O2	Amico	Zone - 1/4 Turn		FAIL	No Intervening Wall Between Zone Valves and Outlets / Inlets Served
46	3rd Floor: Rm 3304 (Pre-Op)	Rm 3304 (Pre-Op)	MA	Amico	Zone - 1/4 Turn		FAIL	No Intervening Wall Between Zone Valves and Outlets / Inlets Served
47	3rd Floor: Rm 3304 (Pre-Op)	Rm 3304 (Pre-Op)	VAC	Amico	Zone - 1/4 Turn		FAIL	No Intervening Wall Between Zone Valves and Outlets / Inlets Served
48	4th Floor: 4352, 4353, 4364, 4365	4352, 4353, 4364, 4365	O2	Amico	Zone - 1/4 Turn		PASS	
49	4th Floor: 4352, 4353, 4364, 4365	4352, 4353, 4364, 4365	MA	Amico	Zone - 1/4 Turn		PASS	
50	4th Floor: 4352, 4353, 4364, 4365	4352, 4353, 4364, 4365	VAC	Amico	Zone - 1/4 Turn		PASS	
51	4th Floor: 4102, 4106, 4114, 4116, 4118, 4120, 4124, 4130, 4144, 4143, 4140, 4154, 4160	4102, 4106, 4114, 4116, 4118, 4120, 4124, 4130, 4144, 4143, 4140, 4154, 4160	O2	Amico	Zone - 1/4 Turn		PASS	
52	4th Floor: 4102, 4106, 4114, 4116, 4118, 4120, 4124, 4130, 4144, 4143, 4140, 4154, 4160	4102, 4106, 4114, 4116, 4118, 4120, 4124, 4130, 4144, 4143, 4140, 4154, 4160	MA	Amico	Zone - 1/4 Turn		PASS	
53	4th Floor: 4102, 4106, 4114, 4116, 4118, 4120, 4124, 4130, 4144, 4143, 4140, 4154, 4160	4102, 4106, 4114, 4116, 4118, 4120, 4124, 4130, 4144, 4143, 4140, 4154, 4160	VAC	Amico	Zone - 1/4 Turn		PASS	
54	4th Floor: 4312, 4316, 4320, 4324, 4326, 4333, 4332, 4346, 4348	4312, 4316, 4320, 4324, 4326, 4333, 4332, 4346, 4348	O2	Amico	Zone - 1/4 Turn		PASS	
55	4th Floor: 4312, 4316, 4320, 4324, 4326, 4333, 4332, 4346, 4348	4312, 4316, 4320, 4324, 4326, 4333, 4332, 4346, 4348	MA	Amico	Zone - 1/4 Turn		PASS	
56	4th Floor: 4312, 4316, 4320, 4324, 4326, 4333, 4332, 4346, 4348	4312, 4316, 4320, 4324, 4326, 4333, 4332, 4346, 4348	VAC	Amico	Zone - 1/4 Turn		PASS	
		5th Floor					NOT IN USE	Rooms 530 - 546 & 507 - 527 Turned Into Offices

TOTAL OUTLETS/ INLETS:	374	TOTAL OUTLETS/INLETS BY SYSTEM GAS:	123	77	7	7	0	160	0	0	0
------------------------------	-----	--	-----	----	---	---	---	-----	---	---	---

OUTLETS, INLETS & MANUFACTURED ASSEMBLY INVENTORY BREAKDOWN:

MANUFACTURER	MODEL	OUTLET/INLET DESCRIPTION	O2	MA	N2O	N2	CO2	VAC	WAGD	IA	Other
Allied	248	Push Pull Release (1 5/8" valve body)) - 1959	6	1				11			
Allied	400	Upper Center Pull Down Release ID Tab - 1976	2	2				2			
Allied	560	500 but DISS	7		7	7		14			
Amico	A1-CH		18	14				24			
Amico	A1-DISS		1					1			
Amico	DISS		48	24				48			
Beacon	B-GEO		1	1				1			
Beacon	D3-DISS		24	24				24			
Hill-Rom	D2-DI		5					6			
Ohio											
Ohio	D2-DISS		11	11				11			
Puritan Bennett	B-DISS							18			

OUTLETS & INLETS: LOCATION & SPECIFICATION							FUNCTION & CONDITION	
#	Area or Zone	Room, Bed or Asset #	System	MFR	Model	Position/Style	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
1	1st Floor	A 103	VAC	Puritan Bennett	B-DISS		PASS	
2	1st Floor	A 105	VAC	Puritan Bennett	B-DISS		PASS	
3	1st Floor	A 108	VAC	Puritan Bennett	B-DISS		PASS	
4	1st Floor	A 109	VAC	Puritan Bennett	B-DISS		PASS	
5	1st Floor	A 110	VAC	Puritan Bennett	B-DISS		PASS	
6	1st Floor	A 111	VAC	Puritan Bennett	B-DISS		PASS	
7	1st Floor	A 112	VAC	Puritan Bennett	B-DISS		PASS	
8	1st Floor	A 114	VAC	Puritan Bennett	B-DISS		PASS	
9	1st Floor	A 115	VAC	Puritan Bennett	B-DISS		PASS	
10	1st Floor	A 118	VAC	Puritan Bennett	B-DISS		PASS	
11	1st Floor	A 119	VAC	Puritan Bennett	B-DISS		PASS	
12	1st Floor	A 120	VAC	Puritan Bennett	B-DISS		PASS	
13	1st Floor	A 126	VAC	Puritan Bennett	B-DISS		PASS	
14	1st Floor	A 128	VAC	Puritan Bennett	B-DISS		PASS	
15	1st Floor	A 131	VAC	Puritan Bennett	B-DISS		PASS	
16	1st Floor	A 133	VAC	Puritan Bennett	B-DISS		PASS	
17	1st Floor	A 135	VAC	Puritan Bennett	B-DISS		PASS	
18	1st Floor	A 136	VAC	Puritan Bennett	B-DISS		PASS	
19	1st Floor	A 153	O2	Hill-Rom	D2-DI		PASS	
20	1st Floor	A 153	VAC	Hill-Rom	D2-DI		PASS	
21	1st Floor	A 153	VAC	Hill-Rom	D2-DI		PASS	
22	1st Floor: ER	A 139 - 1	O2	Hill-Rom	D2-DI		PASS	
23	1st Floor: ER	A 139 - 1	VAC	Hill-Rom	D2-DI		PASS	
24	1st Floor: ER	A 139 - 2	O2	Hill-Rom	D2-DI		PASS	
25	1st Floor: ER	A 139 - 2	VAC	Hill-Rom	D2-DI		PASS	
26	1st Floor: ER	A 139 - 3	O2	Hill-Rom	D2-DI		PASS	
27	1st Floor: ER	A 139 - 3	VAC	Hill-Rom	D2-DI		PASS	
28	1st Floor: ER	A 139 - 4	O2	Hill-Rom	D2-DI		PASS	
29	1st Floor: ER	A 139 - 4	VAC	Hill-Rom	D2-DI		PASS	
30	1st Floor	167	O2	Beacon	B-GEO		PASS	
31	1st Floor	167	MA	Beacon	B-GEO		PASS	
32	1st Floor	167	VAC	Beacon	B-GEO		PASS	
33	2nd Floor	203	O2	Allied	248		PASS	
34	2nd Floor	203	MA	Allied	248		PASS	
35	2nd Floor	203	VAC	Allied	248		PASS	

OUTLETS & INLETS: LOCATION & SPECIFICATION							FUNCTION & CONDITION	
#	Area or Zone	Room, Bed or Asset #	System	MFR	Model	Position/Style	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
36	2nd Floor	207	O2	Allied	400		PASS	
37	2nd Floor	207	O2	Allied	400		PASS	
38	2nd Floor	207	MA	Allied	400		PASS	
39	2nd Floor	207	MA	Allied	400		PASS	
40	2nd Floor	207	VAC	Allied	400		PASS	
41	2nd Floor	207	VAC	Allied	400		PASS	
42	3rd Floor	3315	O2	Amico	A1-CH		PASS	
43	3rd Floor	3315	O2	Amico	A1-CH		PASS	
44	3rd Floor	3315	O2	Amico	A1-CH		PASS	
45	3rd Floor	3315	O2	Amico	A1-CH		PASS	
46	3rd Floor	3315	O2	Amico	A1-CH		PASS	
47	3rd Floor	3315	MA	Amico	A1-CH		PASS	
48	3rd Floor	3315	MA	Amico	A1-CH		PASS	
49	3rd Floor	3315	MA	Amico	A1-CH		PASS	
50	3rd Floor	3315	MA	Amico	A1-CH		PASS	
51	3rd Floor	3315	MA	Amico	A1-CH		PASS	
52	3rd Floor	3315	VAC	Amico	A1-CH		PASS	
53	3rd Floor	3315	VAC	Amico	A1-CH		PASS	
54	3rd Floor	3315	VAC	Amico	A1-CH		PASS	
55	3rd Floor	3315	VAC	Amico	A1-CH		PASS	
56	3rd Floor	3315	VAC	Amico	A1-CH		PASS	
57	3rd Floor	3315B	O2	Amico	A1-CH		PASS	
58	3rd Floor	3315B	O2	Amico	A1-CH		PASS	
59	3rd Floor	3315B	VAC	Amico	A1-CH		PASS	
60	3rd Floor	3315B	VAC	Amico	A1-CH		PASS	
61	3rd Floor	3315B	VAC	Amico	A1-CH		PASS	
62	3rd Floor	3315B	VAC	Amico	A1-CH		PASS	
63	3rd Floor	3315B	VAC	Amico	A1-CH		PASS	
64	3rd Floor	3315D	O2	Amico	A1-CH		PASS	
65	3rd Floor	3315D	O2	Amico	A1-CH		PASS	
66	3rd Floor	3315D	VAC	Amico	A1-CH		PASS	
67	3rd Floor	3315D	VAC	Amico	A1-CH		PASS	
68	3rd Floor	3315D	VAC	Amico	A1-CH		PASS	
69	3rd Floor	3315D	VAC	Amico	A1-CH		PASS	
70	3rd Floor	3315D	VAC	Amico	A1-CH		PASS	

OUTLETS & INLETS: LOCATION & SPECIFICATION							FUNCTION & CONDITION	
#	Area or Zone	Room, Bed or Asset #	System	MFR	Model	Position/Style	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
71	3rd Floor: Pre-Op / Recovery Phase II	3304	O2	Amico	A1-CH		PASS	
72	3rd Floor: Pre-Op / Recovery Phase II	3304	O2	Amico	A1-CH		PASS	
73	3rd Floor: Pre-Op / Recovery Phase II	3304	O2	Amico	A1-CH		PASS	
74	3rd Floor: Pre-Op / Recovery Phase II	3304	O2	Amico	A1-CH		PASS	
75	3rd Floor: Pre-Op / Recovery Phase II	3304	O2	Amico	A1-CH		PASS	
76	3rd Floor: Pre-Op / Recovery Phase II	3304	O2	Amico	A1-CH		PASS	
77	3rd Floor: Pre-Op / Recovery Phase II	3304	O2	Amico	A1-CH		PASS	
78	3rd Floor: Pre-Op / Recovery Phase II	3304	O2	Amico	A1-CH		PASS	
79	3rd Floor: Pre-Op / Recovery Phase II	3304	O2	Amico	A1-CH		PASS	
80	3rd Floor: Pre-Op / Recovery Phase II	3304	MA	Amico	A1-CH		PASS	
81	3rd Floor: Pre-Op / Recovery Phase II	3304	MA	Amico	A1-CH		PASS	
82	3rd Floor: Pre-Op / Recovery Phase II	3304	MA	Amico	A1-CH		PASS	
83	3rd Floor: Pre-Op / Recovery Phase II	3304	MA	Amico	A1-CH		PASS	
84	3rd Floor: Pre-Op / Recovery Phase II	3304	MA	Amico	A1-CH		PASS	
85	3rd Floor: Pre-Op / Recovery Phase II	3304	MA	Amico	A1-CH		PASS	
86	3rd Floor: Pre-Op / Recovery Phase II	3304	MA	Amico	A1-CH		PASS	
87	3rd Floor: Pre-Op / Recovery Phase II	3304	MA	Amico	A1-CH		PASS	
88	3rd Floor: Pre-Op / Recovery Phase II	3304	MA	Amico	A1-CH		PASS	
89	3rd Floor: Pre-Op / Recovery Phase II	3304	VAC	Amico	A1-CH		PASS	
90	3rd Floor: Pre-Op / Recovery Phase II	3304	VAC	Amico	A1-CH		PASS	
91	3rd Floor: Pre-Op / Recovery Phase II	3304	VAC	Amico	A1-CH		PASS	
92	3rd Floor: Pre-Op / Recovery Phase II	3304	VAC	Amico	A1-CH		PASS	
93	3rd Floor: Pre-Op / Recovery Phase II	3304	VAC	Amico	A1-CH		PASS	
94	3rd Floor: Pre-Op / Recovery Phase II	3304	VAC	Amico	A1-CH		PASS	
95	3rd Floor: Pre-Op / Recovery Phase II	3304	VAC	Amico	A1-CH		PASS	
96	3rd Floor: Pre-Op / Recovery Phase II	3304	VAC	Amico	A1-CH		PASS	
97	3rd Floor: Pre-Op / Recovery Phase II	3304	VAC	Amico	A1-CH		PASS	

OUTLETS & INLETS: LOCATION & SPECIFICATION						FUNCTION & CONDITION		
#	Area or Zone	Room, Bed or Asset #	System	MFR	Model	Position/Style	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
98	3rd Floor: PACU	3204	O2	Allied	248		PASS	
99	3rd Floor: PACU	3204	O2	Allied	248		PASS	
100	3rd Floor: PACU	3204	O2	Allied	248		PASS	
101	3rd Floor: PACU	3204	O2	Allied	248		PASS	
102	3rd Floor: PACU	3204	O2	Allied	248		PASS	
103	3rd Floor: PACU	3204	VAC	Allied	248		PASS	
104	3rd Floor: PACU	3204	VAC	Allied	248		PASS	
105	3rd Floor: PACU	3204	VAC	Allied	248		PASS	
106	3rd Floor: PACU	3204	VAC	Allied	248		PASS	
107	3rd Floor: PACU	3204	VAC	Allied	248		PASS	
108	3rd Floor: PACU	3204	VAC	Allied	248		PASS	
109	3rd Floor: PACU	3204	VAC	Allied	248		PASS	
110	3rd Floor: PACU	3204	VAC	Allied	248		PASS	
111	3rd Floor: PACU	3204	VAC	Allied	248		PASS	
112	3rd Floor: PACU	3204	VAC	Allied	248		PASS	
113	3rd Floor	3208	O2	Amico	A1-DISS		PASS	
114	3rd Floor	3208	VAC	Amico	A1-DISS		PASS	
115	3rd Floor	3210	O2	Allied	560		PASS	
116	3rd Floor	3210	VAC	Allied	560		PASS	
117	3rd Floor	3210	VAC	Allied	560		PASS	
118	3rd Floor	3210	N2O	Allied	560		PASS	
119	3rd Floor	3210	N2	Allied	560		NOT IN USE	
	3rd Floor	3210					FAIL	WAGD Inlet Required (Anesthetizing Location)
120	3rd Floor	3218	O2	Allied	560		PASS	
121	3rd Floor	3218	O2	Allied	560		PASS	
122	3rd Floor	3218	VAC	Allied	560		PASS	
123	3rd Floor	3218	VAC	Allied	560		PASS	
124	3rd Floor	3218	VAC	Allied	560		PASS	
125	3rd Floor	3218	VAC	Allied	560		PASS	
126	3rd Floor	3218	N2O	Allied	560		PASS	
127	3rd Floor	3218	N2O	Allied	560		PASS	
128	3rd Floor	3218	N2	Allied	560		NOT IN USE	
129	3rd Floor	3218	N2	Allied	560		NOT IN USE	
	3rd Floor	3218					FAIL	WAGD Inlet Required (Anesthetizing Location)
130	3rd Floor	3232	O2	Allied	560		PASS	
131	3rd Floor	3232	O2	Allied	560		PASS	
132	3rd Floor	3232	VAC	Allied	560		PASS	
133	3rd Floor	3232	VAC	Allied	560		PASS	
134	3rd Floor	3232	VAC	Allied	560		PASS	
135	3rd Floor	3232	VAC	Allied	560		PASS	
136	3rd Floor	3232	N2O	Allied	560		PASS	
137	3rd Floor	3232	N2O	Allied	560		PASS	
138	3rd Floor	3232	N2	Allied	560		NOT IN USE	
139	3rd Floor	3232	N2	Allied	560		NOT IN USE	
	3rd Floor	3232					FAIL	WAGD Inlet Required (Anesthetizing Location)

OUTLETS & INLETS: LOCATION & SPECIFICATION						FUNCTION & CONDITION		
#	Area or Zone	Room, Bed or Asset #	System	MFR	Model	Position/Style	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
140	3rd Floor	3235	O2	Allied	560		PASS	
141	3rd Floor	3235	O2	Allied	560		PASS	
142	3rd Floor	3235	VAC	Allied	560		PASS	
143	3rd Floor	3235	VAC	Allied	560		PASS	
144	3rd Floor	3235	VAC	Allied	560		PASS	
145	3rd Floor	3235	VAC	Allied	560		PASS	
146	3rd Floor	3235	N2O	Allied	560		PASS	
147	3rd Floor	3235	N2O	Allied	560		PASS	
148	3rd Floor	3235	N2	Allied	560		NOT IN USE	
149	3rd Floor	3235	N2	Allied	560		NOT IN USE	
	3rd Floor	3235					FAIL	WAGD Inlet Required (Anesthetizing Location)
150	3rd Floor: Office	3133	O2	Ohio	D2-DISS		UNAVAILABLE	Under Construction
151	3rd Floor: Office	3133	O2	Ohio	D2-DISS		UNAVAILABLE	Under Construction
152	3rd Floor: Office	3133	MA	Ohio	D2-DISS		UNAVAILABLE	Under Construction
153	3rd Floor: Office	3133	MA	Ohio	D2-DISS		UNAVAILABLE	Under Construction
154	3rd Floor: Office	3133	VAC	Ohio	D2-DISS		UNAVAILABLE	Under Construction
155	3rd Floor: Office	3133	VAC	Ohio	D2-DISS		UNAVAILABLE	Under Construction
156	3rd Floor: Office	3134	O2	Ohio	D2-DISS		UNAVAILABLE	Under Construction
157	3rd Floor: Office	3134	O2	Ohio	D2-DISS		UNAVAILABLE	Under Construction
158	3rd Floor: Office	3134	MA	Ohio	D2-DISS		UNAVAILABLE	Under Construction
159	3rd Floor: Office	3134	MA	Ohio	D2-DISS		UNAVAILABLE	Under Construction
160	3rd Floor: Office	3134	VAC	Ohio	D2-DISS		UNAVAILABLE	Under Construction
161	3rd Floor: Office	3134	VAC	Ohio	D2-DISS		UNAVAILABLE	Under Construction
162	3rd Floor	3135	O2	Ohio	D2-DISS		UNAVAILABLE	Under Construction
163	3rd Floor	3135	MA	Ohio	D2-DISS		UNAVAILABLE	Under Construction
164	3rd Floor	3135	VAC	Ohio	D2-DISS		UNAVAILABLE	Under Construction
165	3rd Floor	3137	O2	Ohio	D2-DISS		UNAVAILABLE	Under Construction
166	3rd Floor	3137	O2	Ohio	D2-DISS		UNAVAILABLE	Under Construction
167	3rd Floor	3137	MA	Ohio	D2-DISS		UNAVAILABLE	Under Construction
168	3rd Floor	3137	MA	Ohio	D2-DISS		UNAVAILABLE	Under Construction
169	3rd Floor	3137	VAC	Ohio	D2-DISS		UNAVAILABLE	Under Construction
170	3rd Floor	3137	VAC	Ohio	D2-DISS		UNAVAILABLE	Under Construction
171	3rd Floor	3138	O2	Ohio	D2-DISS		UNAVAILABLE	Under Construction
172	3rd Floor	3138	O2	Ohio	D2-DISS		UNAVAILABLE	Under Construction
173	3rd Floor	3138	MA	Ohio	D2-DISS		UNAVAILABLE	Under Construction
174	3rd Floor	3138	MA	Ohio	D2-DISS		UNAVAILABLE	Under Construction
175	3rd Floor	3138	VAC	Ohio	D2-DISS		UNAVAILABLE	Under Construction
176	3rd Floor	3138	VAC	Ohio	D2-DISS		UNAVAILABLE	Under Construction
177	3rd Floor	3139	O2	Ohio	D2-DISS		UNAVAILABLE	Under Construction
178	3rd Floor	3139	O2	Ohio	D2-DISS		UNAVAILABLE	Under Construction
179	3rd Floor	3139	MA	Ohio	D2-DISS		UNAVAILABLE	Under Construction
180	3rd Floor	3139	MA	Ohio	D2-DISS		UNAVAILABLE	Under Construction
181	3rd Floor	3139	VAC	Ohio	D2-DISS		UNAVAILABLE	Under Construction
182	3rd Floor	3139	VAC	Ohio	D2-DISS		UNAVAILABLE	Under Construction
183	4th Floor	4160	O2	Amico	DISS		PASS	
184	4th Floor	4160	O2	Amico	DISS		PASS	
185	4th Floor	4160	MA	Amico	DISS		PASS	
186	4th Floor	4160	VAC	Amico	DISS		PASS	
187	4th Floor	4160	VAC	Amico	DISS		PASS	
188	4th Floor	4154	O2	Amico	DISS		PASS	
189	4th Floor	4154	O2	Amico	DISS		PASS	
190	4th Floor	4154	MA	Amico	DISS		PASS	
191	4th Floor	4154	VAC	Amico	DISS		PASS	
192	4th Floor	4154	VAC	Amico	DISS		PASS	

OUTLETS & INLETS: LOCATION & SPECIFICATION							FUNCTION & CONDITION	
#	Area or Zone	Room, Bed or Asset #	System	MFR	Model	Position/Style	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
193	4th Floor	4150	O2	Amico	DISS		PASS	
194	4th Floor	4150	O2	Amico	DISS		PASS	
195	4th Floor	4150	MA	Amico	DISS		PASS	
196	4th Floor	4150	VAC	Amico	DISS		PASS	
197	4th Floor	4150	VAC	Amico	DISS		PASS	
198	4th Floor	4143	O2	Amico	DISS		PASS	
199	4th Floor	4143	O2	Amico	DISS		PASS	
200	4th Floor	4143	MA	Amico	DISS		PASS	
201	4th Floor	4143	VAC	Amico	DISS		PASS	
202	4th Floor	4143	VAC	Amico	DISS		PASS	
203	4th Floor	4144	O2	Amico	DISS		PASS	
204	4th Floor	4144	O2	Amico	DISS		PASS	
205	4th Floor	4144	MA	Amico	DISS		PASS	
206	4th Floor	4144	VAC	Amico	DISS		PASS	
207	4th Floor	4144	VAC	Amico	DISS		PASS	
208	4th Floor	4130	O2	Amico	DISS		PASS	
209	4th Floor	4130	O2	Amico	DISS		PASS	
210	4th Floor	4130	MA	Amico	DISS		PASS	
211	4th Floor	4130	VAC	Amico	DISS		PASS	
212	4th Floor	4130	VAC	Amico	DISS		PASS	
213	4th Floor	4124	O2	Amico	DISS		PASS	
214	4th Floor	4124	O2	Amico	DISS		PASS	
215	4th Floor	4124	MA	Amico	DISS		PASS	
216	4th Floor	4124	VAC	Amico	DISS		PASS	
217	4th Floor	4124	VAC	Amico	DISS		PASS	
218	4th Floor	4120	O2	Amico	DISS		PASS	
219	4th Floor	4120	O2	Amico	DISS		PASS	
220	4th Floor	4120	MA	Amico	DISS		PASS	
221	4th Floor	4120	VAC	Amico	DISS		PASS	
222	4th Floor	4120	VAC	Amico	DISS		PASS	
223	4th Floor	4118	O2	Amico	DISS		PASS	
224	4th Floor	4118	O2	Amico	DISS		PASS	
225	4th Floor	4118	MA	Amico	DISS		PASS	
226	4th Floor	4118	VAC	Amico	DISS		PASS	
227	4th Floor	4118	VAC	Amico	DISS		PASS	
228	4th Floor	4116	O2	Amico	DISS		PASS	
229	4th Floor	4116	O2	Amico	DISS		PASS	
230	4th Floor	4116	O2	Amico	DISS		PASS	
231	4th Floor	4116	O2	Amico	DISS		PASS	
232	4th Floor	4116	MA	Amico	DISS		PASS	
233	4th Floor	4116	MA	Amico	DISS		PASS	
234	4th Floor	4116	VAC	Amico	DISS		PASS	
235	4th Floor	4116	VAC	Amico	DISS		PASS	
236	4th Floor	4116	VAC	Amico	DISS		PASS	
237	4th Floor	4116	VAC	Amico	DISS		PASS	
238	4th Floor	4114	O2	Amico	DISS		PASS	
239	4th Floor	4114	O2	Amico	DISS		PASS	
240	4th Floor	4114	O2	Amico	DISS		PASS	
241	4th Floor	4114	O2	Amico	DISS		PASS	
242	4th Floor	4114	MA	Amico	DISS		PASS	
243	4th Floor	4114	MA	Amico	DISS		PASS	
244	4th Floor	4114	VAC	Amico	DISS		PASS	
245	4th Floor	4114	VAC	Amico	DISS		PASS	
246	4th Floor	4114	VAC	Amico	DISS		PASS	
247	4th Floor	4114	VAC	Amico	DISS		PASS	

OUTLETS & INLETS: LOCATION & SPECIFICATION							FUNCTION & CONDITION	
#	Area or Zone	Room, Bed or Asset #	System	MFR	Model	Position/Style	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
248	4th Floor	4108	O2	Amico	DISS		PASS	
249	4th Floor	4108	O2	Amico	DISS		PASS	
250	4th Floor	4108	O2	Amico	DISS		PASS	
251	4th Floor	4108	O2	Amico	DISS		PASS	
252	4th Floor	4108	MA	Amico	DISS		PASS	
253	4th Floor	4108	MA	Amico	DISS		PASS	
254	4th Floor	4108	VAC	Amico	DISS		PASS	
255	4th Floor	4108	VAC	Amico	DISS		PASS	
256	4th Floor	4108	VAC	Amico	DISS		PASS	
257	4th Floor	4108	VAC	Amico	DISS		PASS	
258	4th Floor	4104	O2	Amico	DISS		PASS	
259	4th Floor	4104	O2	Amico	DISS		PASS	
260	4th Floor	4104	O2	Amico	DISS		PASS	
261	4th Floor	4104	O2	Amico	DISS		PASS	
262	4th Floor	4104	MA	Amico	DISS		PASS	
263	4th Floor	4104	MA	Amico	DISS		PASS	
264	4th Floor	4104	VAC	Amico	DISS		PASS	
265	4th Floor	4104	VAC	Amico	DISS		PASS	
266	4th Floor	4104	VAC	Amico	DISS		PASS	
267	4th Floor	4104	VAC	Amico	DISS		PASS	
268	4th Floor	4312	O2	Amico	DISS		PASS	
269	4th Floor	4312	O2	Amico	DISS		PASS	
270	4th Floor	4312	MA	Amico	DISS		PASS	
271	4th Floor	4312	VAC	Amico	DISS		PASS	
272	4th Floor	4312	VAC	Amico	DISS		PASS	
273	4th Floor	4316	O2	Amico	DISS		PASS	
274	4th Floor	4316	O2	Amico	DISS		PASS	
275	4th Floor	4316	MA	Amico	DISS		PASS	
276	4th Floor	4316	VAC	Amico	DISS		PASS	
277	4th Floor	4316	VAC	Amico	DISS		PASS	
278	4th Floor	4320	O2	Amico	DISS		PASS	
279	4th Floor	4320	O2	Amico	DISS		PASS	
280	4th Floor	4320	MA	Amico	DISS		PASS	
281	4th Floor	4320	VAC	Amico	DISS		PASS	
282	4th Floor	4320	VAC	Amico	DISS		PASS	
283	4th Floor	4332	O2	Amico	DISS		PASS	
284	4th Floor	4332	O2	Amico	DISS		PASS	
285	4th Floor	4332	MA	Amico	DISS		PASS	
286	4th Floor	4332	VAC	Amico	DISS		PASS	
287	4th Floor	4332	VAC	Amico	DISS		PASS	
288	4th Floor	4333	O2	Amico	DISS		PASS	
289	4th Floor	4333	O2	Amico	DISS		PASS	
290	4th Floor	4333	MA	Amico	DISS		PASS	
291	4th Floor	4333	VAC	Amico	DISS		PASS	
292	4th Floor	4333	VAC	Amico	DISS		PASS	
293	4th Floor	4324	O2	Amico	DISS		PASS	
294	4th Floor	4324	O2	Amico	DISS		PASS	
295	4th Floor	4324	MA	Amico	DISS		PASS	
296	4th Floor	4324	VAC	Amico	DISS		PASS	
297	4th Floor	4324	VAC	Amico	DISS		PASS	
298	4th Floor	4326	O2	Amico	DISS		PASS	
299	4th Floor	4326	O2	Amico	DISS		PASS	
300	4th Floor	4326	MA	Amico	DISS		PASS	
301	4th Floor	4326	VAC	Amico	DISS		PASS	
302	4th Floor	4326	VAC	Amico	DISS		PASS	

OUTLETS & INLETS: LOCATION & SPECIFICATION							FUNCTION & CONDITION	
#	Area or Zone	Room, Bed or Asset #	System	MFR	Model	Position/Style	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
303	4th Floor	4346	O2	Beacon	D3-DISS	Boom	PASS	
304	4th Floor	4346	O2	Beacon	D3-DISS	Boom	PASS	
305	4th Floor	4346	O2	Beacon	D3-DISS	Boom	PASS	
306	4th Floor	4346	O2	Beacon	D3-DISS	Boom	PASS	
307	4th Floor	4346	MA	Beacon	D3-DISS	Boom	PASS	
308	4th Floor	4346	MA	Beacon	D3-DISS	Boom	PASS	
309	4th Floor	4346	MA	Beacon	D3-DISS	Boom	PASS	
310	4th Floor	4346	MA	Beacon	D3-DISS	Boom	PASS	
311	4th Floor	4346	VAC	Beacon	D3-DISS	Boom	PASS	
312	4th Floor	4346	VAC	Beacon	D3-DISS	Boom	PASS	
313	4th Floor	4346	VAC	Beacon	D3-DISS	Boom	PASS	
314	4th Floor	4346	VAC	Beacon	D3-DISS	Boom	PASS	
315	4th Floor	4348	O2	Beacon	D3-DISS	Boom	PASS	
316	4th Floor	4348	O2	Beacon	D3-DISS	Boom	PASS	
317	4th Floor	4348	O2	Beacon	D3-DISS	Boom	PASS	
318	4th Floor	4348	O2	Beacon	D3-DISS	Boom	PASS	
319	4th Floor	4348	MA	Beacon	D3-DISS	Boom	PASS	
320	4th Floor	4348	MA	Beacon	D3-DISS	Boom	PASS	
321	4th Floor	4348	MA	Beacon	D3-DISS	Boom	PASS	
322	4th Floor	4348	MA	Beacon	D3-DISS	Boom	PASS	
323	4th Floor	4348	VAC	Beacon	D3-DISS	Boom	PASS	
324	4th Floor	4348	VAC	Beacon	D3-DISS	Boom	PASS	
325	4th Floor	4348	VAC	Beacon	D3-DISS	Boom	PASS	
326	4th Floor	4348	VAC	Beacon	D3-DISS	Boom	PASS	
327	4th Floor: ICU	4352	O2	Beacon	D3-DISS	Boom	PASS	
328	4th Floor: ICU	4352	O2	Beacon	D3-DISS	Boom	PASS	
329	4th Floor: ICU	4352	O2	Beacon	D3-DISS	Boom	PASS	
330	4th Floor: ICU	4352	O2	Beacon	D3-DISS	Boom	PASS	
331	4th Floor: ICU	4352	MA	Beacon	D3-DISS	Boom	PASS	
332	4th Floor: ICU	4352	MA	Beacon	D3-DISS	Boom	PASS	
333	4th Floor: ICU	4352	MA	Beacon	D3-DISS	Boom	PASS	
334	4th Floor: ICU	4352	MA	Beacon	D3-DISS	Boom	PASS	
335	4th Floor: ICU	4352	VAC	Beacon	D3-DISS	Boom	PASS	
336	4th Floor: ICU	4352	VAC	Beacon	D3-DISS	Boom	PASS	
337	4th Floor: ICU	4352	VAC	Beacon	D3-DISS	Boom	PASS	
338	4th Floor: ICU	4352	VAC	Beacon	D3-DISS	Boom	PASS	
339	4th Floor: ICU	4353	O2	Beacon	D3-DISS	Boom	PASS	
340	4th Floor: ICU	4353	O2	Beacon	D3-DISS	Boom	PASS	
341	4th Floor: ICU	4353	O2	Beacon	D3-DISS	Boom	PASS	
342	4th Floor: ICU	4353	O2	Beacon	D3-DISS	Boom	PASS	
343	4th Floor: ICU	4353	MA	Beacon	D3-DISS	Boom	PASS	
344	4th Floor: ICU	4353	MA	Beacon	D3-DISS	Boom	PASS	
345	4th Floor: ICU	4353	MA	Beacon	D3-DISS	Boom	PASS	
346	4th Floor: ICU	4353	MA	Beacon	D3-DISS	Boom	PASS	
347	4th Floor: ICU	4353	VAC	Beacon	D3-DISS	Boom	PASS	
348	4th Floor: ICU	4353	VAC	Beacon	D3-DISS	Boom	PASS	
349	4th Floor: ICU	4353	VAC	Beacon	D3-DISS	Boom	PASS	
350	4th Floor: ICU	4353	VAC	Beacon	D3-DISS	Boom	PASS	

OUTLETS & INLETS: LOCATION & SPECIFICATION							FUNCTION & CONDITION	
#	Area or Zone	Room, Bed or Asset #	System	MFR	Model	Position/Style	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
351	4th Floor: ICU	4364	O2	Beacon	D3-DISS	Boom	PASS	
352	4th Floor: ICU	4364	O2	Beacon	D3-DISS	Boom	PASS	
353	4th Floor: ICU	4364	O2	Beacon	D3-DISS	Boom	PASS	
354	4th Floor: ICU	4364	O2	Beacon	D3-DISS	Boom	PASS	
355	4th Floor: ICU	4364	MA	Beacon	D3-DISS	Boom	PASS	
356	4th Floor: ICU	4364	MA	Beacon	D3-DISS	Boom	PASS	
357	4th Floor: ICU	4364	MA	Beacon	D3-DISS	Boom	PASS	
358	4th Floor: ICU	4364	MA	Beacon	D3-DISS	Boom	PASS	
359	4th Floor: ICU	4364	VAC	Beacon	D3-DISS	Boom	PASS	
360	4th Floor: ICU	4364	VAC	Beacon	D3-DISS	Boom	PASS	
361	4th Floor: ICU	4364	VAC	Beacon	D3-DISS	Boom	PASS	
362	4th Floor: ICU	4364	VAC	Beacon	D3-DISS	Boom	PASS	
363	4th Floor: ICU	4365	O2	Beacon	D3-DISS	Boom	PASS	
364	4th Floor: ICU	4365	O2	Beacon	D3-DISS	Boom	PASS	
365	4th Floor: ICU	4365	O2	Beacon	D3-DISS	Boom	PASS	
366	4th Floor: ICU	4365	O2	Beacon	D3-DISS	Boom	PASS	
367	4th Floor: ICU	4365	MA	Beacon	D3-DISS	Boom	PASS	
368	4th Floor: ICU	4365	MA	Beacon	D3-DISS	Boom	PASS	
369	4th Floor: ICU	4365	MA	Beacon	D3-DISS	Boom	PASS	
370	4th Floor: ICU	4365	MA	Beacon	D3-DISS	Boom	PASS	
371	4th Floor: ICU	4365	VAC	Beacon	D3-DISS	Boom	PASS	
372	4th Floor: ICU	4365	VAC	Beacon	D3-DISS	Boom	PASS	
373	4th Floor: ICU	4365	VAC	Beacon	D3-DISS	Boom	PASS	
374	4th Floor: ICU	4365	VAC	Beacon	D3-DISS	Boom	PASS	
	5th Floor						NOT IN USE	Offices - Outlets / Inlets Removed From Service. Dental Clinic Does Not Have Outlets / Inlets.

#	Area or Zone	Room# (Outlets Listed Top to Bottom & Left to Right & Front of Room to Back)	System	Position	Assembly Manufacturer	Joint/DISS Leak Detection & Safe Working Condition			PASS/FAIL	Test/Inspection Date	Recommendation(s) or Comments
				Boom, Pendant, or Retractable Column (From left to right upon entering room)		Ceiling Connections	Outlet Connection	Hose Condition			
1	4th Floor	4365	O ₂	BOOM	Steris HarmonyCare	✓	✓	✓	PASS	1/5/2026	Shared Zone Valve
2	4th Floor	4365	Med Air	BOOM	Steris HarmonyCare	✓	✓	✓	PASS	1/5/2026	Shared Zone Valve
3	4th Floor	4365	Vac	BOOM	Steris HarmonyCare	✓	✓	✓	PASS	1/5/2026	Shared Zone Valve
4	4th Floor	4364	O ₂	BOOM	Steris HarmonyCare	✓	✓	✓	PASS	1/5/2026	Shared Zone Valve
5	4th Floor	4364	Med Air	BOOM	Steris HarmonyCare	✓	✓	✓	PASS	1/5/2026	Shared Zone Valve
6	4th Floor	4364	Vac	BOOM	Steris HarmonyCare	✓	✓	✓	PASS	1/5/2026	Shared Zone Valve
7	4th Floor	4346	O ₂	BOOM	Steris HarmonyCare						Shared Zone Valve - Unable To Test
8	4th Floor	4346	Med Air	BOOM	Steris HarmonyCare						Shared Zone Valve - Unable To Test
9	4th Floor	4346	Vac	BOOM	Steris HarmonyCare						Shared Zone Valve - Unable To Test
10	4th Floor	4353	O ₂	BOOM	Steris HarmonyCare	✓	✓	✓	PASS	1/5/2026	Shared Zone Valve
11	4th Floor	4353	Med Air	BOOM	Steris HarmonyCare	✓	✓	✓	PASS	1/5/2026	Shared Zone Valve
12	4th Floor	4353	Vac	BOOM	Steris HarmonyCare	✓	✓	✓	PASS	1/5/2026	Shared Zone Valve
13	4th Floor	4352	O ₂	BOOM	Steris HarmonyCare	✓	✓	✓	PASS	1/5/2026	Shared Zone Valve
14	4th Floor	4352	Med Air	BOOM	Steris HarmonyCare	✓	✓	✓	PASS	1/5/2026	Shared Zone Valve
15	4th Floor	4352	Vac	BOOM	Steris HarmonyCare	✓	✓	✓	PASS	1/5/2026	Shared Zone Valve

#	Area or Zone	Room# (Outlets Listed Top to Bottom & Left to Right & Front of Room to Back)	System	Position	Assembly Manufacturer	Joint/DISS Leak Detection & Safe Working Condition			PASS/FAIL	Test/Inspection Date	Recommendation(s) or Comments
				Boom, Pendant, or Retractable Column (From left to right upon entering room)		Ceiling Connections	Outlet Connection	Hose Condition			
16	4th Floor	4348	O ₂	BOOM	Steris HarmonyCare						Shared Zone Valve - Unable To Test
17	4th Floor	4348	Med Air	BOOM	Steris HarmonyCare						Shared Zone Valve - Unable To Test
18	4th Floor	4348	Vac	BOOM	Steris HarmonyCare						Shared Zone Valve - Unable To Test

GAS CONTAMINANT TESTING										
#	Area or Zone	Room, Bed or Asset #	System	Particulate <i>(Size - Amount)</i>	Dew Point <i>(°F)</i>	Dew Point <i>(°C)</i>	Odor <i>(Objectionable or Pronounced)</i>	Gaseous <i>(Total nonmethane & halogenated hydrocarbons)</i>	Component Condition / Test Results	Deficiency Detail or Corrective Action Needed/Taken
1	1st Floor	167	O2	None	N/A	N/A	None Detected	None Detected	PASS	
2	3rd Floor	3235	O2	None	N/A	N/A	None Detected	None Detected	PASS	
3	3rd Floor	3235	MA	None	N/A	N/A	None Detected	None Detected	PASS	
4	3rd Floor	3235	N2O	None	N/A	N/A	None Detected	None Detected	PASS	
5	4th Floor	4333	O2	None	N/A	N/A	None Detected	None Detected	PASS	
6	4th Floor	4333	MA	None	-24.0 °F	-31.1 °C	None Detected	None Detected	PASS	

System Gas:	Nitrous Oxide				
Manifold Location:	Manifold Room				
Area(s) of Facility Served:	Entire Facility				
MFR	Amico	Change-Over Actuation	110 PSI	Line Pressure (Source Valve)	51 PSI
Model	M2LT-D-HHH-U-N2O	Left Bank Reading		Line Pressure (Main Valve)	N/A
Serial #	20010109-E	Right Bank Reading		Flexible Connectors Date of MFR	Unknown
# of L Header Connections	3	Left Intermediate Regulator Reading			
# of R Header Connections	3	Right Intermediate Regulator Reading			
# of L Cylinders Connected	3	Left Final Line Regulator Reading			
# of R Cylinders Connected	3	Right Final Line Regulator Reading			
Inspection Check List		Inspection Results	Deficiency Detail or Corrective Action Needed/Taken		
Manifold location meets design and construction requirements, is a dedicated enclosure/room and, if outside, meets required separation distances and is installed according to manufacturer specification		PASS			
Cylinders secured, handled and stored appropriately		PASS			
Room/enclosure properly ventilated		PASS			
Constructed with two equal headers, each with enough connections for one average day's supply (minimum 2 per header), tied to final line pressure assembly so either header can supply system		PASS			
Final, intermediate & header (if applicable) relief valves are in correct location, vented outside, have correct pressure/pipe size and are turned down and screened		PASS			
Automatic means of alternation/properly alternates		PASS			
Valves, flexible connectors & regulators free of leaks		PASS			
Flexible connectors gas-specific & less than 5 years old		SEE ANNEX	Per Manufacturer's Recommendations, Pigtails Should Be Replaced Every 5 Years		
Local signal properly indicates operating status		PASS			
Labeling is present and correct on source valve, main valve, visible distribution piping, visible relief piping, cylinders, door & manifold		PASS			

System Gas:	Nitrogen				
Manifold Location:	Manifold Room				
Area(s) of Facility Served:	Entire Facility				
MFR	Amico	Change-Over Actuation	150 PSI	Line Pressure (Source Valve)	165 PSI
Model	M2HD-D-HH-U-NIT	Left Bank Reading		Line Pressure (Main Valve)	N/A
Serial #	20000327-B	Right Bank Reading		Flexible Connectors Date of MFR	Unknown
# of L Header Connections	3	Left Intermediate Regulator Reading			
# of R Header Connections	3	Right Intermediate Regulator Reading			
# of L Cylinders Connected	3	Left Final Line Regulator Reading			
# of R Cylinders Connected	3	Right Final Line Regulator Reading			
Inspection Check List		Inspection Results	Deficiency Detail or Corrective Action Needed/Taken		
Manifold location meets design and construction requirements, is a dedicated enclosure/room and, if outside, meets required separation distances and is installed according to manufacturer specification		PASS			
Cylinders secured, handled and stored appropriately		PASS			
Room/enclosure properly ventilated		PASS			
Constructed with two equal headers, each with enough connections for one average day's supply (minimum 2 per header), tied to final line pressure assembly so either header can supply system		PASS			
Final, intermediate & header (if applicable) relief valves are in correct location, vented outside, have correct pressure/pipe size and are turned down and screened		PASS			
Automatic means of alternation/properly alternates		PASS			
Valves, flexible connectors & regulators free of leaks		PASS			
Flexible connectors gas-specific & less than 5 years old		SEE ANNEX	Per Manufacturer's Recommendations, Pigtails Should Be Replaced Every 5 Years		
Local signal properly indicates operating status		PASS			
Labeling is present and correct on source valve, main valve, visible distribution piping, visible relief piping, cylinders, door & manifold		PASS			

Compressor System Gas:		Medical Air							
Compressor System Location:		Mechanical Room Penthouse							
Area(s) of Facility Served:		Entire Facility							
System MFR	Amico	Comp #1 HRS	13852			Dryer System 1		Dew Point Monitor	
System Model #	A-RED-D-120P-TL-N-050-20863-A	Comp #2 HRS	4315			Type	Desiccant	MFR	Powerex
System Serial #	(H)11/13/2007-3538853-33.34					MFR	Amico	Model	PDPM1001AJ
Compressor Type	Oilless Reciprocating					Model	U-482-38	Reading	-13.0 °F
Compressor MFR	Amico					Reading		Accuracy Checked	
Compressor SCFM						Dryer System 2		Carbon Monoxide Monitor	
Motor HP	5					Type	Desiccant	MFR	Amico
Lead Cut In / Out (psi)	80 / 100					MFR	Amico	Model	A310
Lag Cut In / Out (psi)	70 / 90					Model	U-482-38	Reading	0 ppm
Main Line Pressure (psi)	50					Reading		Calibrated	
Inspection Check List			Inspection Results		Deficiency Detail or Corrective Action Needed/Taken				
System, source & main valves, visible distribution and relief piping labeled			PASS						
Compressor system is located in a dedicated mechanical equipment area that is adequately ventilated, has all required utilities, and maintains ambient temperature recommended by MFR			PASS						
System has required components, compressors meet specification and all component are in good repair and functioning properly			PASS						
Aftercoolers, where required, meet specification and are in good repair			PASS						
Receiver is of sufficient capacity, corrosion-resistant construction, complies with ASME VIII, and is equipped with a pressure relief valve, automatic drain, manual drain, sight glass and pressure indicator			PASS						
Dryers are sized properly, comprised of required components and produce air at/below required maximum dew point per requirements			PASS						
Filters properly located and installed, constructed per the manufacturer, meet efficiency requirements for application and are not in need of changing			PASS						
Piping arrangement, redundancies & standby header (if applicable) meet requirements and are in good repair			PASS						
Electrical power and controls meet requirements and are in good repair			PASS						
Compressor intake is in compliant location and intake end is protected per requirements			PASS						
Operating alarms and local signals are in place and properly functioning			PASS						
Dew point reading is accurate when compared to calibrated monitor reading			PASS						
CO reading is accurate and monitor has been calibrated (if applicable)			PASS						

Vacuum/WAGD System Gas:	Medical-Surgical Vacuum				
Vacuum/WAGD System Location:	Mechanical Room Penthouse				
Area(s) of Facility Served:	Entire Facility				
System MFR	Amico	Pump #1 HRS	41046		
System Model #	V-RVL-D-200P-TS-N-075-20863-M	Pump #2 HRS	40008		
System Serial #	500409				
Pump/Producer Type	Lubricated Rotary Vane				
Pump/Producer MFR	Busch				
Pump/Producer SCFM					
Motor HP	7.5				
Lead Cut In / Out (inHg)	20 / 24				
Lag Cut In / Out (inHg)	18 / 13				
Main Line Pressure (inHg)	-23				

Inspection Check List	Inspection Results	Deficiency Detail of Corrective Action Needed/Taken
Vacuum/WAGD system meets requirements for specific application and located appropriately	PASS	
Vacuum/WAGD system has required components, pumps (if applicable) meet specification and all components are properly functioning and in good repair	PASS	Note: Pump #2 Turned Off. Service Is In Process.
Receiver (if applicable) complies with ASME VIII, is capable of withstanding 60psi gauge pressure and 30inHg, is equipped with a manual drain and is of sufficient capacity	PASS	
Filters properly located, arranged and installed, constructed per the manufacturer, meet efficiency requirements for the application, are in good repair and are not in need of changing	PASS	
Piping arrangement and redundancies meet requirements and components are in good repair	PASS	
Electrical power and controls meet requirements and properly functioning	PASS	
Operating alarms and local signals are in place and properly functioning	PASS	
Exhaust is in compliant location and end is protected per requirements	PASS	
Vacuum/WAGD system, source & main valves, visible distribution & exhaust piping properly labeled	PASS	

Cryogenic Fluid System Type:	Oxygen		
Cryogenic Fluid System Location:	Behind Maintenance		
Area(s) of Facility Served:	Entire Facility		
Bulk Supplier/System Owner	Messer	Number of EOSCs	1
Primary Liquid Level		EOSC Location(s)	Dock Area
Primary Vessel Pressure		Number of IBERs	0
Secondary Liquid Level		IBER Location(s)	N/A
Secondary Vessel Pressure		# of IBER Header Connections	N/A
# of Reserve Header Connections		# of IBER Cylinders Connected	N/A
# of Reserve Cylinders Connected		IBER Header Pressure	N/A
Reserve Header Pressure			
Pressure at Source Valve	50 PSI		
Pressure at Main Valve	50 PSI		

Inspection Check List	Inspection Results	Deficiency Detail of Corrective Action Needed/Taken
Cryogenic fluid system is located appropriately and location meets requirements	PASS	
Cryogenic fluid system has required components, meets specification and all components are properly functioning and in good repair	PASS	
Cryogenic fluid system main & reserve supply and fill system meet specification and all components are properly functioning and in good repair	PASS	
Vaporizers meet specification, are functioning properly and in good repair	PASS	
Cryogenic fluid system components including high-pressure manifolds, pressure control devices, pressure relief devices, tubing and valves meet specification, are functioning properly and in good repair	PASS	
Required alarms are in place, properly functioning and in good repair	PASS	
Cryogenic fluid systems has an auxiliary source connection which meets requirements and in good repair	PASS	
An EOSC is located in each required location, meets specifications and is in good repair	PASS	
An IBER is located in each required location, meets specifications and is in good repair	N/A	

ANNEX (RECOMMENDATIONS & FUTURE PLANNING)

The following components have been found to out of compliance with current codes and standards for new installations, however due to the provisions of NFPA 99 5.1.1.4, these may continue to remain in use as long as the Authority Having Jurisdiction (AHJ) has not deemed these a distinct hazard to life. EMS has included the following recommendations for how to address these issues of compliance in the future. The nature of this Annex is informational only and does not constitute these components as deficient.

GENERAL RECOMMENDATIONS

Component Category	Recommendation	Status
Flexible Connections (Booms, columns, etc.)	Per NFPA 99 5.1.14, EMS recommends inspecting all manufactured assemblies employing flexible connections at least every 18 months	Complete
Utility System Distribution Mapping	Per TJC EC 02.05.01, EMS recommends updating existing medical gas system utility map (if any) to current medical gas distribution piping arrangement	N/A
Maintenance Personnel Training	Per NFPA 99 5.1.14, EMS recommends all personnel involved in the maintenance and operating of medical gas system components receive training per one of the three acceptable training requirements	N/A
EOSC Function Testing	Per ASSE 2021 D.3.6 - Periodically inspect and test EOSC for proper operation	Complete

MASTER ALARMS

Occurrence Location(s)	Reference Number(s)	Gas System(s)	Manufacturer(s)	Comment/Recommendation	# of Occurrences
ER, Maintenance, 4th Floor	7, 8, 10, 25, 26, 28, 37, 38, 40	O2	Amico	Tested by Bulk Supplier	9
ER, Maintenance, 4th Floor	9, 27, 39	O2	Amico	Alarm Not Required (Liq x Gas)	3

AREA ALARMS

Occurrence Location(s)	Reference Number(s)	Gas System(s)	Manufacturer(s)	Comment/Recommendation	# of Occurrences
------------------------	---------------------	---------------	-----------------	------------------------	------------------

VALVES

Occurrence Location(s)	Reference Number(s)	Gas System(s)	Manufacturer(s)	Comment/Recommendation	# of Occurrences
0	0	0	0	No Nitrogen Valve Installed Serving OR 3218; N2 Outlets Not In Service	1
0	0	0	0	No Nitrogen Valve Installed Serving OR 3210; N2 Outlets Not In Service	1
3rd Floor: OR 3218, 3rd Floor: OR 3232, 3rd Floor: OR 3235, 3rd Floor: 302 - 313 (Master Shut Off - Box 1), 3rd Floor: 302 - 313 (Master Shut Off - Box 2), 3rd Floor: 3204 (Recovery), 3rd Floor: OR 3208, 3rd Floor: OR 3210	12, 13, 14, 15, 16, 17, 18, 19, 20, 29, 30, 31, 32, 33, 34, 37, 38, 39	O2, VAC, N2O	NCG	No Pressure Indicator: Verify Year Of Install & Determine By Risk Assessment If Corrections Are Required To Meet Current Standard	18

OUTLETS & INLETS

Occurrence Location(s)	Reference Number(s)	Gas System(s)	Manufacturer(s)	Comment/Recommendation	# of Occurrences
------------------------	---------------------	---------------	-----------------	------------------------	------------------

GAS CONTAMINANTS

Occurrence Location(s)	Sample Outlet/Port	Reference Number(s)	Gas System(s)	Comment/Recommendation	# of Occurrences
------------------------	--------------------	---------------------	---------------	------------------------	------------------

SOURCE EQUIPMENT

GAS CYLINDER MANIFOLDS

System Type / Area(s) Served	Checklist Item	Comment/Recommendation
Nitrogen Manifold serving Entire Facility	Flexible connectors gas-specific & less than 5 years old	Per Manufacturer's Recommendations, Pigtails Should Be Replaced Every 5 Years
Nitrous Oxide Manifold serving Entire Facility	Flexible connectors gas-specific & less than 5 years old	Per Manufacturer's Recommendations, Pigtails Should Be Replaced Every 5 Years
